Original / Duplicate / Triplicate

CONTRACT CERTIFICATE

SBR.No

No. 1st and Final Bill
Division : RR Nagar Division (For Other Works) Date.....20.....
Estimate Cost (Rs.) :-50.00 Lakhs Sub-Division : Yashwanthapura -Sub Division
Bill Received No .....Dated.....Cash Book Voucher No.....dated.....
Scheduled Docket No: Head of Account : P- 3294 D.R. No:
Name of Work (as per sanctioned estimate): Construction of Toilets Insides JP Park In Ward No 17

AEE/YPR/SBR/DR/13/22-23 Dt:-14/11/2022

Job Code:-017-20-0000017
Name of Contractor and Full Address: **Rangashamaiah,**
Reference to Agreement No /Wo No: EE/RRND/Wo.No/000116 Dt:-10/12/2020

Certified that the measurements were taken by me on 08/02/2022 and recorded of Pages No 667672 667670 of measurement Book No : 6647/1 and that the work is satisfactorily executed.

Rangesha mai
Signature of Contractor

08/02/2022
Officer-in-charge of work

Certified that the measurements were taken by me on.....and found correct. The work is satisfactorily executed.

Certified that the quantities of materials shown in column 3 of Account II have been actually brought to site of the work and the contractor has not previously received any advance on this security. These materials are of an imperishable nature and are all required for immediate use on the work in connection with items for finished work have been agreed upon. A normal agreement signed and executed by the contractor is recorded in the office.

If Memorandum of Payment

Sub Divisional Officer
Executive Engineer
ASST. EXECUTIVE ENGINEER
Yeshwanthpura Sub Division
Bruhat Bangalore Mahanagara Palike

1)	Total value of work done or supplies made as per account within	₹ - 42,86,956 -
2)	Deduct amount to be held in reserve being.....percent Rs.....	
3)	" Balance	
4)	Deduct Payment :	
	a) Amount of previous payment as in the Office Cash Book Voucher No.....Dated.....S.D No.....	GST@12% (+) 5,14,434 -
		48,01,390 -
	Amount adjusted towards cash advance recovery of	IT - 42870
		CGST - 42870
	b) Payments cost store or other materials supplied.	SGST - 42870
	Now made recovery of amount creditable to this/other work Amount paid on this bill Cheque/Cash	(-) 4,14,517 -
		LR - 21,250
5)	Balance being unpaid value of work done held in reserve	CESS - 4287
6)	Deduct cash advance made on the office Cash Book Voucher No..... date .....less adjustments	UCC - 42870
7)	Net amount due to or from contractor Unadjusted items	SD - 21,4500
8)	Advance to contractor for materials brought to site (as detailed) within value of Government materials supplied	By cheque - 4386873 -

Rangesha mai
Contractor's Signature

Received Rs... .....(in works)
.....

By Cash and by adjustment of Payment as per memorandum.
Witnesses:
1.
2.

(For use in the Office)

Rangesha mai
Dated..... **Signature of Contractor**

Paid by me by cheque No..... Dated.....

Cash Rs..... Dated.....
Initials of Officer Making Payment

Audited and admitted for Rs. 48,01,390 -
Passed by Cheque for Rs. 4386873 -
(Forty three lakh eighty six thousand eight hundred and seventy three only)
by adjustment 4,14,517 -
Executive Engineer

Accounts Superintendent
Rajarajeshwari Engg.
Asst. Engineer

Scanned with CamScanner

1	ground manually (other than foundation of buildings, culverts, road drains and trenches of pipe lines and cables) and removing the excavated stuff to a distance not exceeeding 50 m and lift upto 1.5m, excavated surface levelled and neatly dressed, disposed earth to be levelled after breaking of clods and nealty dressed as per specifications Complete as per the direction of Engineer in Charge with all lead and Lift	Cum	8.83	173.00	0.00	0.00	8.83	1527.00	8.83	1527.00
2	Earthwork excavation for foundation of buildings, culverts, water supply, sanitary lines and electrical conduits either in pits or in trenches 1.5m and above in width, in ordinary soil not exceeding 1.5m in depth including dressing the bottom and sides of pits and trenches, stacking the excavated soil clear from edges of excavation with lead upto 50m. after breaking of clods complete as per specifications.Complete as per the direction of Engineer in Charge with all lead and Lift	Cum	299.50	329.00	0.00	0.00	299.50	98536.00	299.50	98536.00
	Above 125 %	Cum	345.22	329.38	0.00	0.00	345.22	113709.00	345.22	113709.00
3	KSRB 4-1.3 : Providing and laying in position plain cement concrete of mix M7.5 with OPC cement @ 180 kgs, with 40mm and down size graded granite metal coarse aggregates @ 0.85 cum and fine aggregates @ 5.75 cum machine mixed, concrete laid in layers not exceeding 15 cms, thick, well compacted, in foundation and plinth, including cost of all materials, labour, HOM of machinery, curing complete as per specification.	Cum	34.50	5,500.00	0.00	0.00	34.50	189750.00	34.50	189750.00
	Above 125 %	Cum	7.82	6,031.57	0.00	0.00	7.82	47155.00	7.82	47155.00
4	Providing and laying in position reinforced cement concrete of design mix M20 with OPC cement @320kgs, with 20mm and down size graded granite metal coarse aggregates @ 0.878cum and fine aggregates @ 0.459cum, with superplastisiser @ 3lts confirming to IS9103-1999 Reaffirmed-2008, machine mixed, concrete laid in layers not exceeding 15cms thick, vibrated for all works in foundation plinth and ground floor level for roof slabs, staircase, lintles, retaining walls, return walls, walla (any thickness) including attached plasters, columns, piers, abutments, pillars, posts, structs, buttresses, string or lacing courses, parpets, coping, bed blocks, anchor, plain window cills, fillets etc., including cost of all materials, labour, HOM of machinery, curing complete as per specification. Complete as per the direction of Engineer in Charge with all lead and Lift	Cum	7.62	6,500.00	0.00	0.00	7.62	49524.00	7.62	49524.00
5	Providing and removing centering, shuttering, strutting, propping etc., an removal of form work for sides & soffits of beams, beam hauncing cantilever girders, bressumers & lintels & not exceeding 1.0 in depth including cost of all materials, labour complete as per specifications.	Sqm	135.91	350.00	0.00	0.00	135.91	47570.00	135.91	47570.00
6	Providing and laying in position reinforced cement cocnrete of design mix M20 with OPC cement @ 27.20 Kgs with 12mm & down sizes graded grantie metal coarse aggregated @ 0.5865 cum & fine aggregates, @ 0.391 Cum with super super plastisiser @ 0.225 Ltrs maichine mixed well compacted plain chajja 8.50 Cms avg thickness, up to ground floor level including removing centering, shuttering, strutting, propping etc., and removal of form work for cost of all materials, laobur HOM of machinary, curing complete as per specification.Ground floor	Sqm	8.13	485.00	0.00	0.00	8.13	3941.00	8.13	3941.00
	Above 125 %	Sqm	5.27	539.53	0.00	0.00	5.27	2842.00	5.27	2842.00

Scanned with CamScanner

7	tieng with binding wire and anchoring to the adjoining members wherever necessary, complete as per design (laps, hooks and wastage shall not be measured and paid) cost of all materials, labour, HOM of machineries etc., complete as per specifications. Specification No.KBS 4.6.3. FOR TMT Bars Fe- 500 Ground Floor Complete as per the direction of Engineer in Charge with all lead and Lift	Tonne	2.84	79,000.00	0.00	0.00	2.84	224093.00	2.84	224093.00
8	Providing & Constructing Granite/ trap/basalt size stone Masonary in basement with Cement morter 1:8 edges of stone chistle dressed in courses not less than 15 cms high, bond stones at two mtr apart in each course including cost of all materials, labour, curing complete as per specifications Complete as per the direction of Engineer in Charge with all lead and Lift	Cum	40.29	6,200.00	0.00	0.00	40.29	249817.00	40.29	249817.00
9	Filling available excavated earth (excluding rock) in sides of foundations upto plinth in layers not exceeding 20 cms. In depth, compacting each deposited layer by ramming after watering with lead upto 50 m. and lift upto 1.5m. Inluding cost of all labour complete as per speicifications.Complete as per the direction of Engineer in Charge with all lead and Lift	Cum	119.88	220.00	0.00	0.00	119.88	26373.00	119.88	26373.00
	Above 125 %	Cum	476.13	221.42	0.00	0.00	476.13	105425.00	476.13	105425.00
10	Providing and constructing Pre cast solid blocks with Compressive strength not less than 35 kg/ sqm with cement morter 1:4 masonary (quion, Jamb, closer block) with solid concrete blockx of size 40 x 15 x 20 cms confirming to IS 2185/1965 in super structures including cost of materials, labour charges, scaffolding, curing complete as per specifications. Complete as per the direction of Engineer in Charge with all lead and Lift.	Sqm	106.70	1,000.00	0.00	0.00	106.70	106695.00	106.70	106695.00
11	Providing & constructing non load bearing walls cemect concrete solid blocks with compressive strength not less than 35 kg/sqm with cement morter 1:4 (jamb, closer blocks) with blocks of size 40X10X20. (LXBXH) confirming to I.S. : 2185/1965 in super structure including cost of materials, labour charges, scaffolding, curing complete as per specification.Complete as per the direction of Engineer in Charge with all lead and Lift.	Sqm	37.88	950.00	0.00	0.00	37.88	35981.00	37.88	35981.00
	Above 125 %	Sqm	42.21	902.74	0.00	0.00	42.21	38105.00	42.21	38105.00
12	Providing 18mm thick cement plaster in single coat with cement mortor 1:3 to Brick masonary including rounding off corners wherver required smooth rendering,: Providing and removing scaffolding, including cost of materials, labour, curing complete as per specifications. Complete as per the direction of Engineer in Charge with all lead and Lift	Sqm	204.86	310.00	0.00	0.00	204.86	63507.00	204.86	63507.00
13	Providing 18mm thick cement plaster in single coat with cement mortor 1:4, to brick masonry including rounding off corners wherver required smooth rendering,: Providing and removing scaffolding, including cost of materials, labour, curing complete as per specifications.(internal). Complete as per the direction of Engineer in Charge with all lead and Lift	Sqm	399.90	288.00	0.00	0.00	399.90	115170.00	399.90	115170.00

Original / Duplicate / Triplicate

Scanned with CamScanner

	14	Providing and removing scaffolding, including cost of materials, labour, curing complete as per specifications. GG. Complete as per the direction of Engineer in Charge with all lead and Lift. Complete as per the direction of Engineer in Charge with all lead and Lift	Sqm	180.07	298.00	0.00	0.00	180.07	53661.00	180.07	53661.00
	15	Providing INTEGRAL CRYSTALINE Waterproofing treatment to the sunken portion of toilets. Using Crystalline Slurry of approved make @ 1.40 kg per SQM in two coats (0.7 Kg per coat) confirming to ASTM S 1202 & DINV 18998 standards. Complete as per the direction of Engineer in Charge with all lead and Lift.	Sqm	188.84	500.00	0.00	0.00	188.84	94420.00	188.84	94420.00
	16	Providing and fixing of factorymade 30 mm P.V.C door frame of size 50x47 mm with a wall thickness of 5 mm made out of extrued 5 mm rigid PVC foamsheet metered cut at cornwers & jointed 2 nos 150 mm long brackets of 15 x 15 mm MS Square tube, the entire door frame to be reinforced with 19 x 19 m square tube of 19 gauge. the door frame to be fixed to the wall using MS screws of 65 /80 mm size complete as per manufacturers specification& directions of Engineer in charge. Complete as per the direction of Engineer in Charge with all lead and Lift	Sqm	51.30	520.00	0.00	0.00	51.30	26676.00	51.30	26676.00
	17	Providing & fixing 30mm thick factory made rigid foam Panelled Door Shutters made from M.S. tube of 19 gauge thickness, size 19 x 19mm for styles and 15 x 15mm for top and bottom rails, covered with heat moulded PVC channel of 5mm thick sheet & 30 x 50mm wide to form styles & 5mm thick & 75mm wide PVC Sheets for top rail, lock rail & bottom rail on either side & 5mm thick 20mm wide PVC sheet as gap insert for top rail & bottom rail, Panelling of 5mm thick PVC sheet fitted in the M.S. Frame, Sealed to the styles & rails with 5 x 30mm PVC sheet beading on either side & joined together with solvent cement adhesive etc., Complete as per manufacturers specification & direction of Engineer-in-charge fixed to frames with 3 nos of 75 mm Aluminium hinges. GG. Complete as per the direction of Engineer in Charge with all lead and Lift	Sqm	14.18	2,600.00	0.00	0.00	14.18	36855.00	14.18	36855.00
	18	Providing ceramic tiles of approved make, shade and size for flooring, treads of steps and landings laid on a bed of 12mm thick cement mortor 1:3 mix, flush pointing with white cement using colour pigment, including cost of materials, labour, curing, complete as per specifications. size 30x30cms. Complete as per the direction of Engineer in Charge with all lead and Lift	Sqm	209.63	1,340.00	0.00	0.00	209.63	280904.00	209.63	280904.00
	19	Providing skirting, dado, rises of steps with colour glazed tiles on 10mm thick cement plaster 1:3 and jointed with white cement slurry over rough plaster surface (excluding cost of rough plastered surface which should be measured and paid separately) using glazed tiles of approved make and size including cost of materials, labour, complete as per specifications. Complete as per the direction of Engineer in Charge with all lead and Lift	Sqm	100.63	1,405.00	0.00	0.00	100.63	141378.00	100.63	141378.00
			Sqm	255.85	1,400.13	0.00	0.00	255.85	358224.00	255.85	358224.00
		Above 125 %									

Scanned with CamScanner

20	Providing and applying two coats with of bonus washable distemper of approved brand and shade on wall surface including priming coat with distemper primer matter including preparing the surface free from mortar drops and other foreign materials, labour, complete as per specifications. Complete as per the direction of Engineer in Charge with all lead and Lift.	Sqm	399.90	120.00	0.00	0.00	399.90	47987.00	399.90	47987.00
21	Water proof cement paint KSRB 15-16.1 : Providing and finishing external walls in two coats with waterproof cement paint with primer of approved brand and shade to give an even shade after throughly brooming the surface to remove all dirt and loose powdered material, free from mortar drops and other foreign matter cost of materials, labour, complete as per specifications. (P.No.124/15.53.2) --do with Primer-- GG. Complete as per the direction of Engineer in Charge with all lead and Lift	Sqm	204.86	112.00	0.00	0.00	204.86	22944.00	204.86	22944.00
22	Providing and fixing white vitreous china clay, water closet Indian type (Squatting pan) of size 580mm with footrests, 100mm S or P trap, (approved make) cutting and making good the wall and floor wherever required, including cost of materials, labour complete as per specifications. Complete as per the direction of Engineer in Charge with all lead and Lift	Each	14.00	1,466.00	0.00	0.00	14.00	20524.00	14.00	20524.00
23	Providing and fixing white vitreous china clay, flat back, lipped front urinal basin of 430x260x350mm with 5 litres PVC automatic flushing cistern, C.I / M.S brackets, standard flush pipe and C.P. brass spreaders with brass unions and G.I. clamps complete painting of fittings and brackets, cutting and making good the wall and floor wherever required, including cost of materials, labour complete as per specifications. Complete as per the direction of Engineer in Charge with all lead and Lift	Each	14.00	3,200.00	0.00	0.00	14.00	44800.00	14.00	44800.00
24	Providing & fixing CI Nahani trap of approved make confirming to ISI specification and construction of cistren in M 15 as per directions. Complete as per the direction of Engineer in Charge with all lead and Lift	Each	10.00	270.00	0.00	0.00	10.00	2700.00	10.00	2700.00
25	Providing and fixing white vitreous china clay, flat back wash basin size 550x400mm with a single 15mm C.P brass pillar tap with C.I / M.S brackets, 32 mm C.P. brass waste of standard pattern, painting of fittings and brackets, cutting and making good the wall and floor wherever required, including cost of materials, labour complete as per specifications. Complete as per the direction of Engineer in Charge with all lead and Lift	Nos	10.00	3,328.00	0.00	0.00	10.00	33280.00	10.00	33280.00
	Providing and fixing to wall, ceiling and floor , Medium density polyethylene pipes	Mtrs	20.00	359.00	0.00	0.00	20.00	7180.00	20.00	7180.00
	6.00 kgf /sqcm working pressure	Mtrs	45.00	327.18	0.00	0.00	45.00	14723.00	45.00	14723.00
26	Above 125 %	Mtrs	35.00	419.00	0.00	0.00	35.00	14665.00	35.00	14665.00
	Providing and fixing to wall, ceiling and floor , Medium density polyethylene pipes	Mtrs	27.00	359.12	0.00	0.00	27.00	9696.00	27.00	9696.00
	6.00 kgf /sqcm working pressure	Mtrs	25.00	496.00	0.00	0.00	25.00	12400.00	25.00	12400.00
27	Above 125 %	Mtrs	47.00	418.61	0.00	0.00	47.00	19675.00	47.00	19675.00
	Providing and fixing to wall, ceiling and floor , Medium density polyethylene pipes									
28	6.00 kgf /sqcm working pressure									
	Above 125 %									

Scanned with CamScanner

29	CPVC) pipes conforming to IS 15778, having thermal stability for hot and cold water supply including all cpvc plain and brasss threaded fittings including fixing thepipes with the clamp at 1.00mtr spacing . This includes joining of pipes fittings with one set of cpvc solvent cement and testing of joints complete (Internal works) (Concealed work including cutting chases and good the walls etc.)A)15mm dia pipe nominal OD pipes Complete as per the direction of Engineer in Charge with all lead and Lift	Mtrs	15.00	227.00	0.00	0.00	15.00	3405.00	15.00	3405.00
	Above 125 %	Mtrs	75.00	226.93	0.00	0.00	75.00	17020.00	75.00	17020.00
30	Providing and fixing to wall, ceiling and floor chlorinated poly vinyl chloride (CPVC) pipes conforming to IS 15778, having thermal stability for hot and cold water supply including all cpvc plain and brasss threaded fittings including fixing thepipes with the clamp at 1.00mtr spacing . This includes joining of pipes fittings with one set of cpvc solvent cement and testing of joints complete (Internal works) (Concealed work including cutting chases and good the walls etc.) B)20 mm dia pipe nominal OD pipes Complete as per the direction of Engineer in Charge with all lead and Lift	Mtrs	50.00	259.00	0.00	0.00	50.00	12950.00	50.00	12950.00
	Above 125 %	Mtrs	75.00	258.88	0.00	0.00	75.00	19416.00	75.00	19416.00
31	Providing and fixing in position brass gate valve with C.I wheel of approved quality (screwed end) NB including cost of all materials, labour and HOM of equipments with all leads complete as per specifications. Specification no: KBS 13.2.6/ a) of 20mm dia. Complete as per the direction of Engineer in Charge with all lead and Lift	Nos	15.00	360.00	0.00	0.00	15.00	5400.00	15.00	5400.00
	Above 125 %	Nos	13.00	370.14	0.00	0.00	13.00	4812.00	13.00	4812.00
32	Providing and fixing in position brass gate valve with C.I wheel of approved quality (screwed end) NB including cost of all materials, labour and HOM of equipments with all leads complete as per specifications. Specification no: KBS 13.2.6/ b) of 25mm dia. Complete as per the direction of Engineer in Charge with all lead and Lift	Nos	10.00	485.00	0.00	0.00	10.00	4850.00	10.00	4850.00
	Above 125 %	Nos	10.00	494.62	0.00	0.00	10.00	4946.00	10.00	4946.00
33	Supplying water storage tanks made of virgin polymer (LLDPE) with two layers outer Black or Blue and inner White layer of approved quality and make, conforming to I.S.I./ISO/SSI specifications. Complete as per the direction of Engineer in Charge with all lead and Lift	Nos	1,000.00	5.00	0.00	0.00	1000.00	5000.00	1000.00	5000.00
	Above 125 %	Nos	4,000.00	5.60	0.00	0.00	4000.00	22385.00	4000.00	22385.00
34	Providing and fixing to wall, ceiling and floor chlorinated poly vinyl chloride (CPVC) pipes conforming to IS 15778, having thermal stability for hot and cold water supply including all cpvc plain and brasss threaded fittings including fixing thepipes with the clamp at . This includes joining of pipes fittings with one set of cpvc solvent cement and testing of joints complete (External works) 25 mm dia pipe nominal OD pipes. Complete as per the direction of Engineer in Charge with all lead and Lift	mtrs	100.00	197.00	0.00	0.00	100.00	19700.00	100.00	19700.00
	Above 125 %	mtrs	398.00	160.83	0.00	0.00	398.00	64012.00	398.00	64012.00
35	Providing stone ware gully trap of approved quality and fixing in C C 1:2:4 and plastering with C M 1:3 where ever necessary (Rate including cost of all materials, fixtures and lead). Size: 15 cm x 10 cm. Complete as per the direction of Engineer in Charge with all lead and Lift	Each	10.00	209.00	0.00	0.00	10.00	2090.00	10.00	2090.00
	Above 125 %	Each	10.00	209.30	0.00	0.00	10.00	2093.00	10.00	2093.00

Scanned with CamScanner

		bricks of class designation 50 in cement mortar 1:5, C.I cover with frame (light duty) 455x450 mm internal dimensions, total weight of cover with frame to be not less than 38 kg (weight of cover 23kg and weight of frame 15 kg) R.C.C. top slab											
36		with cement concrete M15 with 20mm and downsize granite metal, foundation bed concrete complete as per standard design including cost of materials, labour charges, curing complete as per specifications. Complete as per the direction of Engineer in Charge with all lead and Lift	Nos	8.00	8,568.85	0.00	0.00	8.00	68551.00	8.00	68551.00
		Providing and fixing self-supported, ribbed, high quality, high grade (D:350 MPAYst Min), pre- painted Galvalume steel roof sheet, coatedwith bare Galvalume thickness as specified for differentspans with a tolerance of+/- 0.02 mm, according to technical specificationconfirming to A 792, with NCCA11-1, or ECCAT4 Pencil hardness HB,NCCA standard T-Bend test. The roof should be fastened to thegutterbeam, on the external sloping side, at an interval of 51mm Centre											
EIRL -1		toCentre, to a depth of 65 mm with GI anchor bolts and neoprenewashers & subjecting the gutter beam to Schmidt, Hammer test toensure the anchorage of the anchor bolts. The self-supported roofingsystem should be designed to with stand the wind loacl (As per IS 875part-3) & Earthquake load (as per IS 1893) &the design should alsocomply with any other technical requirements such as turbo ventilatorsof 0.60 mts. dia and skylights of size 4.26 x 0.60 mts. fixed one in each row @ 10.00 Mtr C/C alongthe length & hangers for electrical fixturesas per the requirements including cost of all materials &labour forerection, all lead and lift, loading and unloading, HOM of machineriesetc.,complete as per the standard	Sqm	73.98	1,718.50	0.00	0.00	73.98	127130.00	73.98	127130.00
		Fabrication supplying and erecting M.S. tubular trusses of all spans as Kg per approved drawing & design with prefabricated steel applications usingquality material and are durable, reliable and corrosion and abrasionresistant. Welding shall confirm to latest structural welding code. Qualityshall be on various											
EIRL -2		parameters like shape, size, design gauge andpolish. The entire trusses is anchored in RCC column by using 4 nosof M.S. anchor bolts at each support with 10mm thick base plate andshoe plate. The work includes cutting, straightening, placing in positionM.S. pipes and welding wherever necessary and applying one coat ofredoxide primer coat to all the members including cost of all materials,labour charges, and hire charges of machineries for cutting, welding,grinding and erection equipments, with all lead and lift, transportation,letc., complete as per specification	Sqm	4,438.65	122.28	0.00	0.00	4438.65	542747.00	4438.65	542747.00
		KSRB 7.1 : Providing and fixing in position collapsible steel shutters Sqm with											
EIRL -3		single or double leaf with vertical channel 20mmx10mmx2mmh braced with flat iron diagonals 20mmx5mm size, with top and bottom rails of T iron sections of 40x40x6 mm with 38mm dia steel pulleys complete with bolt and nuts, locking arrangements, stoppers, handles on both sides with 7.5cms openings at 10 cms. c to c applying a priming coat of red lead paint, cost of materials, labour, HOM complete as per specifications, size of gate 2.4mx1.4m	Sqm	13.86	5,739.34	0.00	0.00	13.86	79547.00	13.86	79547.00

Scanned with CamScanner

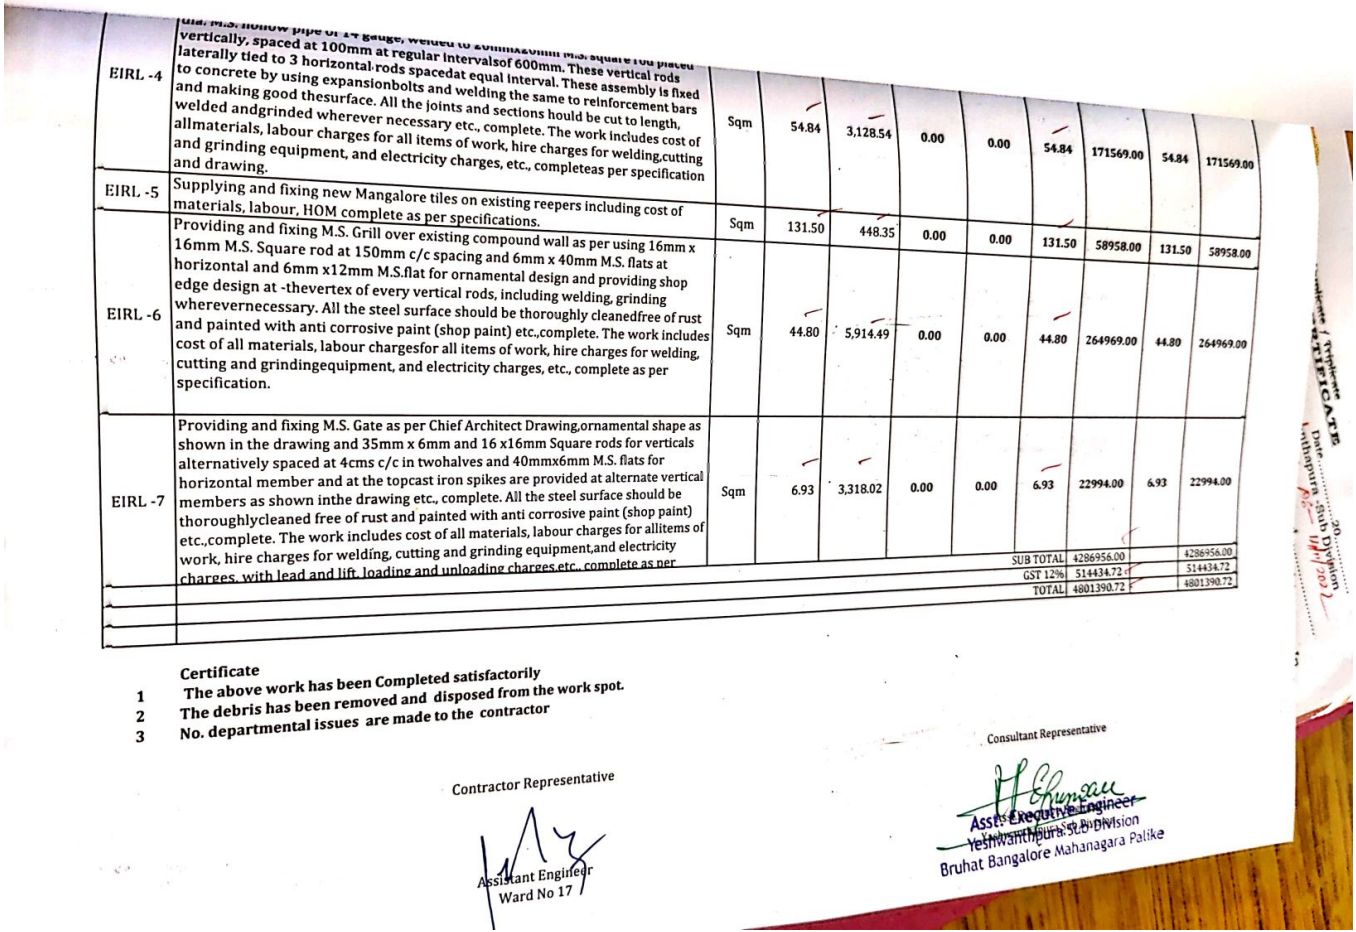

EIRL -4	dia. M.S. hollow pipe of 14 gauge, welded to 20mmx20mm M.S. square rod placed vertically, spaced at 100mm at regular intervalsof 600mm. These vertical rods laterally tied to 3 horizontal rods spacedat equal interval. These assembly is fixed to concrete by using expansionbolts and welding the same to reinforcement bars and making good thesurface. All the joints and sections hould be cut to length, welded andgrinded wherever necessary etc., complete. The work includes cost of allmaterials, labour charges for all items of work, hire charges for welding,cutting and grinding equipment, and electricity charges, etc., completeas per specification and drawing.	Sqm	54.84	3,128.54	0.00	0.00	54.84	171569.00	54.84	171569.00
EIRL -5	Supplying and fixing new Mangalore tiles on existing reepers including cost of materials, labour, HOM complete as per specifications.	Sqm	131.50	448.35	0.00	0.00	131.50	58958.00	131.50	58958.00
EIRL -6	Providing and fixing M.S. Grill over existing compound wall as per using 16mm x 16mm M.S. Square rod at 150mm c/c spacing and 6mm x 40mm M.S. flats at horizontal and 6mm x12mm M.S.flat for ornamental design and providing shop edge design at -thevertex of every vertical rods, including welding, grinding wherevernecessary. All the steel surface should be thoroughly cleanedfree of rust and painted with anti corrosive paint (shop paint) etc.,complete. The work includes cost of all materials, labour chargesfor all items of work, hire charges for welding, cutting and grindingequipment, and electricity charges, etc., complete as per specification.	Sqm	44.80	5,914.49	0.00	0.00	44.80	264969.00	44.80	264969.00
EIRL -7	Providing and fixing M.S. Gate as per Chief Architect Drawing,ornamental shape as shown in the drawing and 35mm x 6mm and 16 x16mm Square rods for verticals alternatively spaced at 4cms c/c in twohalves and 40mmx6mm M.S. flats for horizontal member and at the topcast iron spikes are provided at alternate vertical members as shown inthe drawing etc., complete. All the steel surface should be thoroughlycleaned free of rust and painted with anti corrosive paint (shop paint) etc.,complete. The work includes cost of all materials, labour charges for allitems of work, hire charges for welding, cutting and grinding equipment,and electricity charges, with lead and lift, loading and unloading charges,etc., complete as per	Sqm	6.93	3,318.02	0.00	0.00	6.93	22994.00	6.93	22994.00
							SUB TOTAL	4286956.00		4286956.00
							GST 12%	514434.72		514434.72
							TOTAL	4801390.72		4801390.72

Certificate

1 **The above work has been Completed satisfactorily**
2 **The debris has been removed and disposed from the work spot.**
3 **No. departmental issues are made to the contractor**

Contractor Representative

Assistant Engineer
Ward No 17

Consultant Representative

Asst. Executive Engineer
Yeshwanthpura Sub Division
Bruhat Bangalore Mahanagara Palike

CERTIFICATE
Date 26/10/2022
Yeshwanthpura Sub Division

Scanned with CamScanner
